PALLAVI BOREWELL & DRILLERS

Dealers in : 6½" 4½" Borewells Drilling & Inwell Drilling
All Kinds of Motors & Pumps, Sales & Service
No. 66/8, 1st Main Road, Maruthi Layout, M. G. Road,
Nelamangala Bangalore - 562 123.
Moble : 93412 24311, 90089 87530,



Ref : *Date : 24.2.2014*

YIELD REPORT

1. Name and Address of the Party : AEE Ward No 15 Dasarahalli Sub Division BBMP.
2. Borewell Location : Kalasahi nagar (Temple Corner)
3. Total Depth Drilled : 1141 Feet
4. Casing Pipe : 259 Feet
5. Coupling : 13 callers
6. Yield Details :
   a) First Spring Touched at : 290 Feet
   b) Second Spring Touched at : 545 Feet
   c) Third Spring Touched at : 960 Feet
7. Total Yield in G.P.H. : 1200 G.P.H
8. Remarks : Yield is Good

AB-15

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಟಿ.ದಾಸರಹಳ್ಳಿ ಉಪ-ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ. ಬಿಬಿಎಂಪಿ
ಬೆಂಗಳೂರು

For PALLAVI BOREWELL & DRILLERS

M.B. Niranjan
Proprietor

I.g permit:- L

A. N. CHOWDHARY, M.Sc.,
GEOLOGIST

Phone :
Cell : 98454 73398

SRI SHIRDI SAI CONSULTANTS

10, 3rd Floor, 19th Cross, 14th Main, Revenue Layout, Padamanabhanagar
Bangalore - 560 061.

GROUND WATER INVESTIGATION REPORT

S. No. : To the ASSE Executive Engineer - BBMP Dasarahalli Sub Division - Date : 24-2-2014

1. Name of the Customer Ward NO:- 15

a) Village Kaliagamma Temple Dice Roads b) Block / Taluk. c) District Bangalore

2. Location.

3. Lithology of the Area Granetic in nature -

4. Tophographic Features of the Area The area was a plain land

5. Hydrogeological condition of the Area Good -

6. Geophysical survey result. By Diving method

   a) Type of Method.

   b) No of Soundings Conducted.

   c) Recommended Sounding.

   d) Particulars of formations present in the subsurface/possible ground water zones encountered at

Around 400' 9
680-730' } 2
900-940' }

   e) Condition of Ground Water. Good

7. Type of well Recommended. Bore well (6½") -

8. Depth Recommended. 950 - 1000' -

9. Expected Yield. 1400 - 1600 GPH -

10. Quality of Water. Good -

AB-15

11. Approximate depth at which the water is expected to be met. Around 400' 9

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬಿ.ದಾಸರಹಳ್ಳಿ ಉಪ-ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ, ಬಿಬಿಎಂಪಿ
ಬೆಂಗಳೂರು

12. Recommended Type and Length of casing to be inserted. Nearly 160-190' GI MS casing may be needed

13. Rain water Harvesting adviced or not Strictly Advices -

14. Remarks.

Site Plan Map

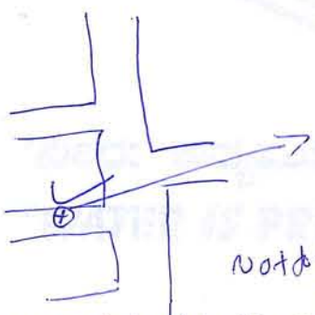

Signature of the consultant

Note :- The Survey was carried out by this divining / Geophysical method of surveying is with our good knowledge and experience. However no guarantee of water will be given.
